

03/04/2019

Beard Construction

Allotment News letter



Mr Fox has taken up residence under the scaffolding


We have been on site for 33 weeks and progress has been good to date, we have scaffolded out 5 blocks which is approximately 400 tonne of materials which has been carried by hand from the road to the location



We have moved forward with the water attenuation from the Castle mill roof area – drainage checked, and new silt trap delivered – they are sealed connections so should not leak



New signage has been supplied and installed at roof level and on the down pipes to hopefully make all aware of the water collection system

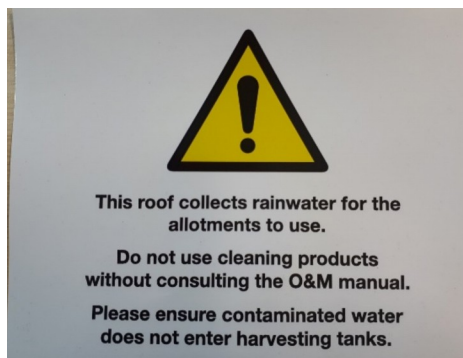

Badger activity on the north of the site in January on the last snow days

Two badgers have been seen in the run.

Over the next couple of months we be completing the 4 blocks on the north end of the site and removing scaffolding which will progress to the south end of the site, scaffolding having been erected on blocks F and G (3&4) which will allow works on the outsides to progress, Decorations, Brise Soleil, Window changes etc.



Works to the badger run have recommenced from the 1st April – setting out of the steelwork in preparation for the steel delivery and erection next week 8th April - steelwork progress barring any problems 3-4 weeks

Regards Paul Renton-Rose
